Barry Dock Transport Interchange Programme - Clause 32

ID	Task Name	Duration	Start	Finish
1	**C2280 - Barry Dock Transport Interchange**	**104 days**	**Tue 22/11/22**	**Wed 03/05/23**
2	**Key Dates**	**104 days**	**Tue 22/11/22**	**Wed 03/05/23**
3	Contract Award	0 days	Tue 22/11/22	Tue 22/11/22
4	Site Access	0 days	Mon 09/01/23	Mon 09/01/23
5	Works Commence	0 days	Mon 16/01/23	Mon 16/01/23
6	Planned Completion Date	0 days	Wed 26/04/23	Wed 26/04/23
7	Terminal Float	4 days	Thu 27/04/23	Wed 03/05/23
8	Contract Completion Date	0 days	Wed 03/05/23	Wed 03/05/23
9	**Preconstruction Works**	**15 days**	**Tue 22/11/22**	**Mon 12/12/22**
10	Produce Construction H&S Plan	15 days	Tue 22/11/22	Mon 12/12/22
11	Produce CTMP	15 days	Tue 22/11/22	Mon 12/12/22
12	Produce CEMP	15 days	Tue 22/11/22	Mon 12/12/22
13	Produce CDM CPP	15 days	Tue 22/11/22	Mon 12/12/22
14	Produce QPs	15 days	Tue 22/11/22	Mon 12/12/22
15	Produce ITPs	15 days	Tue 22/11/22	Mon 12/12/22
16	Produce Waste Management Plans	15 days	Tue 22/11/22	Mon 12/12/22
17	Agree Working Method	15 days	Tue 22/11/22	Mon 12/12/22
18	Boundary Treatments Temporary Works Design	10 days	Tue 22/11/22	Mon 05/12/22
19	Design Approval	5 days	Tue 06/12/22	Mon 12/12/22
20	**Lead ins**	**70 days**	**Tue 22/11/22**	**Mon 13/03/23**
21	ABP	44 days	Tue 22/11/22	Fri 03/02/23
22	ABP Install	3 days	Wed 15/02/23	Mon 20/02/23
23	WPD Payment	24 days	Tue 22/11/22	Fri 23/12/22
24	WPD	30 days	Mon 09/01/23	Fri 17/02/23
25	WPD Install	2 days	Mon 20/02/23	Tue 21/02/23
26	Downstream Defender Units	30 days	Tue 22/11/22	Mon 16/01/23
27	W&W Utilities	57 days	Tue 22/11/22	Wed 22/02/23
28	Works	3 days	Thu 23/02/23	Mon 27/02/23
29	Flow Restrictor Unit	20 days	Tue 22/11/22	Mon 19/12/22
30	Street lighting procurement	70 days	Tue 22/11/22	Mon 13/03/23
31	**Construction Works**	**76 days**	**Mon 09/01/23**	**Wed 26/04/23**
32	**Site Setup**	**3 days**	**Mon 09/01/23**	**Wed 11/01/23**
33	Setup Site Compound	3 days	Mon 09/01/23	Wed 11/01/23
34	Erect Herras Fencing	3 days	Mon 09/01/23	Wed 11/01/23
35	Install Traffic Management System & Pedestrian Diversions	1 day	Mon 09/01/23	Mon 09/01/23
36	**Traffic Management Phase**	**76 days**	**Mon 09/01/23**	**Wed 26/04/23**
37	Maintained Access to top carpark	25 days	Mon 09/01/23	Fri 10/02/23
38	Area inaccessable	33 days	Mon 13/02/23	Wed 29/03/23
39	Access post surfacing works	18 days	Thu 30/03/23	Wed 26/04/23
40	**Site Clearance**	**4 days**	**Thu 12/01/23**	**Tue 17/01/23**
41	Remove Ironworks	1 day	Thu 12/01/23	Thu 12/01/23
42	Remove Existing Railing, Signage, Lighting and Bolla	2 days	Thu 12/01/23	Fri 13/01/23
43	Remove Existing Vegetation/Trees	2 days	Mon 16/01/23	Tue 17/01/23
44	Remove Kerbs and Edging	2 days	Thu 12/01/23	Fri 13/01/23
45	**Existing Drainage Repos & Survey**	**22 days**	**Mon 13/02/23**	**Tue 14/03/23**
46	CCTV Survey	2 days	Mon 13/02/23	Tue 14/02/23
47	Proposed Internal Repairs	10 days	Wed 15/02/23	Tue 28/02/23
48	Proposed External Repairs	10 days	Wed 01/03/23	Tue 14/03/23
49	**Retaining Wall (4 Phases)**	**14 days**	**Tue 17/01/23**	**Fri 03/02/23**
50	Excavation to formation	4 days	Tue 17/01/23	Fri 20/01/23
51	Blinding Concrete	4 days	Wed 18/01/23	Mon 23/01/23
52	Install Drainage	4 days	Fri 20/01/23	Wed 25/01/23
53	FRC Foundation	7 days	Thu 19/01/23	Fri 27/01/23
54	Construct wall	6 days	Wed 25/01/23	Wed 01/02/23
55	Reinstatement behind wall	6 days	Fri 27/01/23	Fri 03/02/23
56	**Earthworks**	**45 days**	**Mon 16/01/23**	**Fri 17/03/23**
57	Remove Surfacing & Stone	7 days	Mon 16/01/23	Tue 24/01/23
58	Excavate to Formation	22 days	Thu 19/01/23	Fri 17/02/23
59	Lay membrane	32 days	Wed 25/01/23	Thu 09/03/23
60	Place imported stone	32 days	Wed 25/01/23	Thu 09/03/23
61	**Drainage**	**20 days**	**Thu 26/01/23**	**Wed 22/02/23**
62	Install Attenuation Tank	5 days	Thu 26/01/23	Wed 01/02/23
63	Install Outflow Control Chambers	5 days	Thu 02/02/23	Wed 08/02/23
64	Install downstream defender units	3 days	Thu 02/02/23	Mon 06/02/23
65	Install flow restrictor unit	2 days	Thu 02/02/23	Fri 03/02/23
66	Interconnect Pipework & Chambers	10 days	Thu 09/02/23	Wed 22/02/23
67	**Ducting**	**5 days**	**Thu 23/02/23**	**Wed 01/03/23**
68	Install Ducts & Drawpits	5 days	Thu 23/02/23	Wed 01/03/23
69	**Kerbing**	**12 days**	**Thu 02/03/23**	**Fri 17/03/23**
70	Prep & lay HB	7 days	Thu 02/03/23	Fri 10/03/23
71	Prep & Lay Edging	5 days	Mon 13/03/23	Fri 17/03/23
72	**Pavement Construction**	**37 days**	**Thu 02/03/23**	**Tue 25/04/23**
73	**Main Carriageway**	**37 days**	**Thu 02/03/23**	**Tue 25/04/23**
74	Sub base	7 days	Thu 02/03/23	Fri 10/03/23
75	Final Trim	3 days	Mon 13/03/23	Wed 15/03/23
76	Base course	3 days	Thu 16/03/23	Mon 20/03/23
77	Binder course	3 days	Tue 21/03/23	Thu 23/03/23
78	Surface course	2 days	Fri 21/04/23	Mon 24/04/23
79	Surface Course - Pedestrian Crossing Points	1 day	Tue 25/04/23	Tue 25/04/23
80	**Footways**	**20 days**	**Mon 20/03/23**	**Tue 18/04/23**
81	Block Paving	16 days	Mon 20/03/23	Wed 12/04/23
82	Tactile Paving	2 days	Thu 13/04/23	Fri 14/04/23
83	Footway Surfacing	2 days	Mon 17/04/23	Tue 18/04/23
84	**Roundabout Tie In**	**2 days**	**Wed 19/04/23**	**Thu 20/04/23**
85	Binder Course	1 day	Wed 19/04/23	Wed 19/04/23
86	Surface Course	1 day	Thu 20/04/23	Thu 20/04/23
87	**Finishing Works**	**30 days**	**Tue 14/03/23**	**Wed 26/04/23**
88	Install street lighting	18 days	Mon 20/03/23	Fri 14/04/23
89	Install street lighting - roundabout area	10 days	Tue 14/03/23	Mon 27/03/23
90	Install Street Furniture - bins & motorcycle stands	2 days	Wed 19/04/23	Thu 20/04/23
91	Install Signage	4 days	Wed 19/04/23	Mon 24/04/23
92	Install benches	2 days	Wed 05/04/23	Thu 06/04/23
93	Install cycle shelters	1 day	Wed 19/04/23	Wed 19/04/23
94	Install Bus Stops	4 days	Mon 03/04/23	Thu 06/04/23
95	Lay New Road Markings	2 days	Tue 25/04/23	Wed 26/04/23
96	Landscaping	22 days	Fri 24/03/23	Wed 26/04/23
97	**Completion**	**0 days**	**Wed 26/04/23**	**Wed 26/04/23**
98	As-Built Information	0 days	Wed 26/04/23	Wed 26/04/23
99	Handover	0 days	Wed 26/04/23	Wed 26/04/23

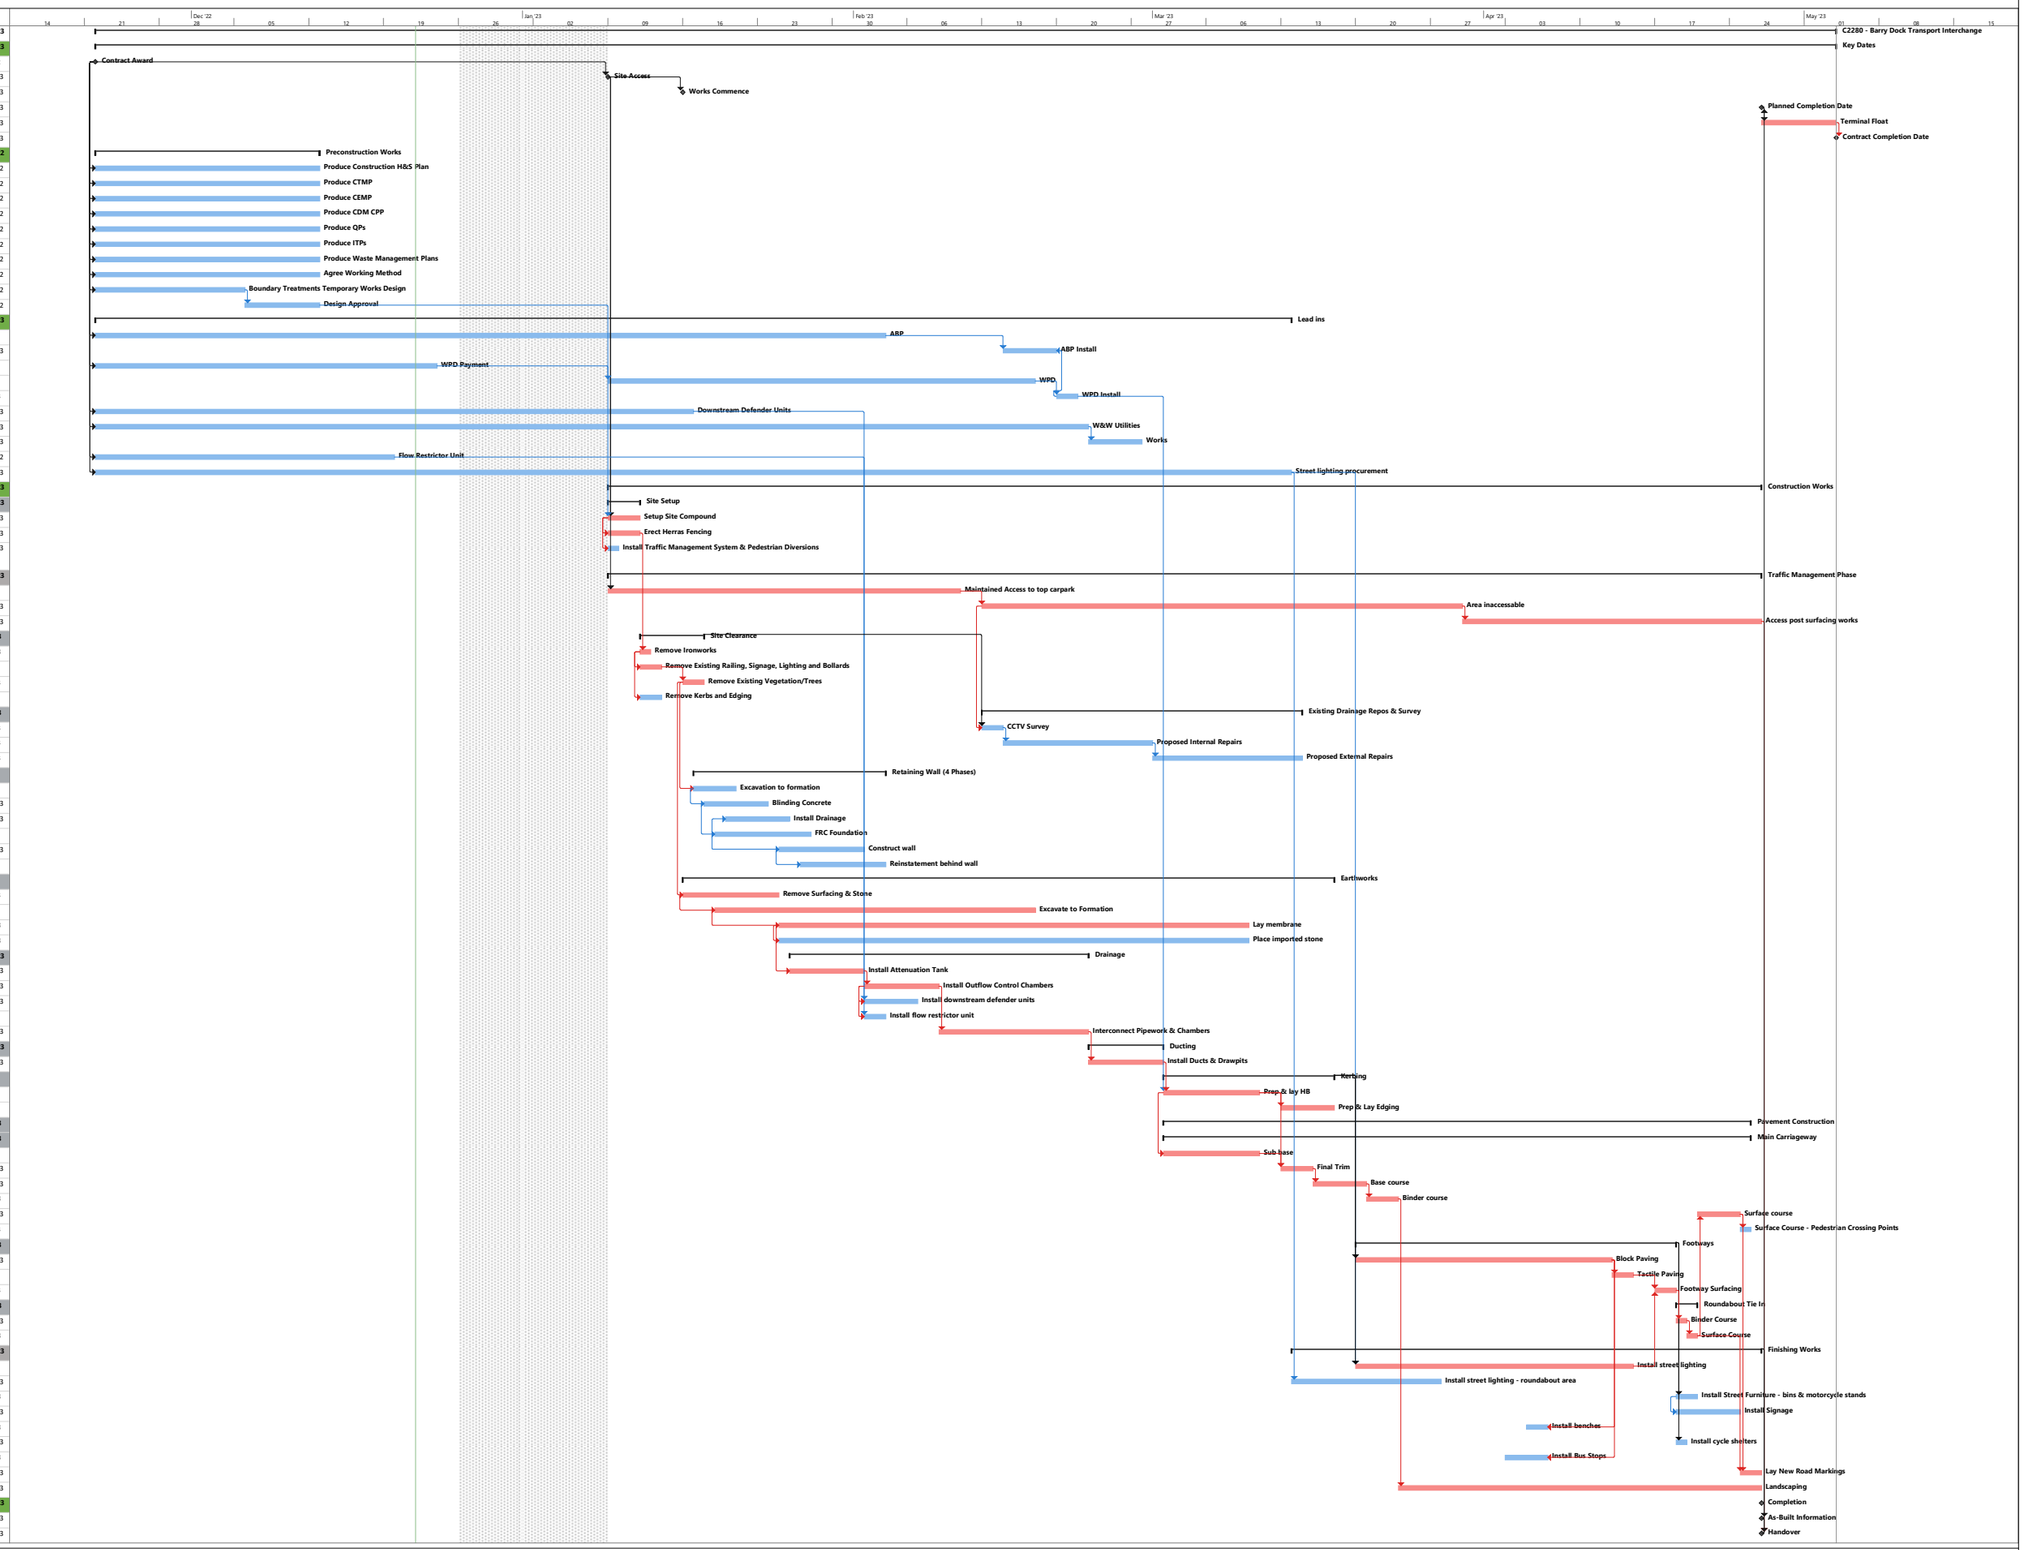

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

Author: Mike Davies Printed: Thu 22/12/22 11:10

Barry Dock Transport Interchange Programme - Clause 32



Author: Mike Davies Printed: Thu 22/12/22 11:10
